

qr 9/18/24


CONSOLIDATED QUARTERLY REPORT ON GOVERNMENT PROJECTS, PROGRAMS or ACTIVITIES

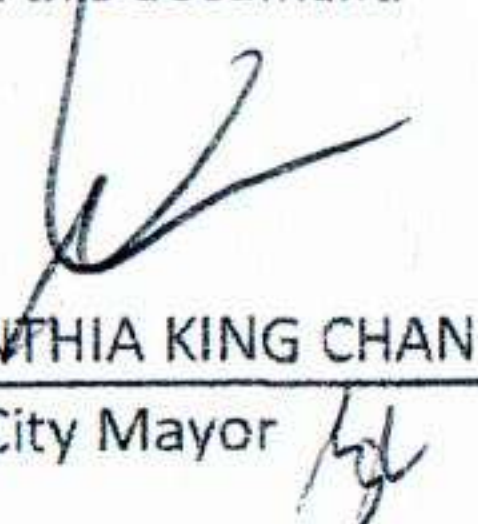
REGION: 7 CALENDAR YEAR 2025
 PROVINCE: CEBU QUARTER: 2
 CITY/MUNICIPALITY: LAPULAPU CITY

Program or Project	Location	Total Cost	Date Started	Target Completion Date	Project Status		No. of Extensions, if any	Remarks
					% of Completion	Total Cost Incurred to Date		
1. Repair and Improvement of Garbage Holding Center at Lapulapu City Public Market (PH 2)	Poblacion	998,282.97	31/07/2024	26/10/2024	100.00%	996,445.39		Completed
2. Completion/Upgrade/Repair of Lapulapu City Health Center	Pusok	1,908,248.57	17/05/2024	06/11/2024	100.00%	1,900,875.67		Completed
3. Rehabilitation and Upgrade of Pangan-an Multi-Purpose/ Evacuation Center	Pangan-an	4,905,358.88	17/05/2024	11/01/2025	100.00%	4,967,028.65		Completed
4. Completion of roofing at Lapulapu City College	Gun-ob	551,200.00	26/06/2020	24/08/2020	90.00%	496,080.00		Suspended
5. Construction of Caubian Barangay Hall	Caubian	4,789,416.44	04/04/2019	08/10/2019	90.00%	718,412.47		Suspended due to lot problem

We hereby certify that we have reviewed the contents and hereby attest to the veracity and correctness of the data or information contained in this document.


 JUDITH D. FURUTA
 City Budget Officer


 HELEN G. DUNGOG
 City Accountant


 MA. CYNTHIA KING CHAN
 City Mayor
